


02.11.2024



Dr. Ernest Rip Patton, Jr. North Nashville Transit Center

This Transit Center is a new WeGo development at 26th Avenue and Clarksville Highway. It will have an air-conditioned waiting room, restrooms, Wi-Fi, and multiple bus bays to connect several routes across town. It is part of an overall effort to increase access to public transit across Nashville while reducing the necessity of transferring Downtown at the Elizabeth Duff Transit Center at WeGo Central.

Project Update

Building Area

- Rooftop units have been set on roof and are currently being connected to the ductwork system.
- Storefront framing and glass install are at 100 percent in preparation of door hardware.

Plaza Area


- All structural steel for the paratransit canopy in the plaza has been erected. Metal decking at the canopy will be installed prior to conduit being run for exterior lighting.
- Sidewalks to the plaza have been poured, and structural soil will be placed before landscaping begins.

Bus Lanes

- At canopies A, B, C, E1, and E2, conduit has been pulled and installed in preparation for canopy lights along the drive aisle.
- Curb and gutter, along with concrete pavement, is about 90 percent complete in the bus lanes.

Right of Way

- Nashville Electric Service (NES) has installed both power poles along Clarksville Pike, in efforts to secure permanent power.
- The erection of structural steel is ongoing at both the inbound and outbound canopy locations. Sidewalks along the inbound location on Clarksville Pike intersecting at 26th Avenue are about 75 percent complete in preparation for reopening.

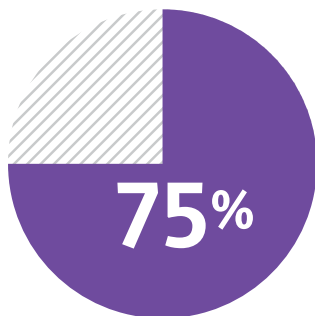

Work Progress
